


# LIFT UPDATE

## Lift Project Reaches Final Stage

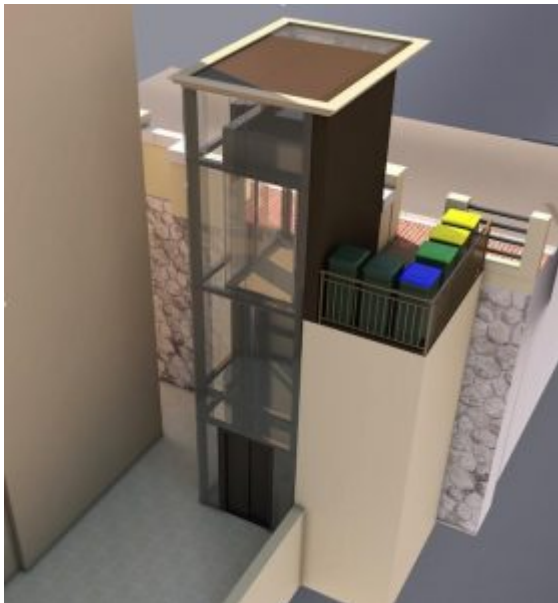

Churchwarden, Tim Humphreys is pleased to report that lift project is at last reaching its final stage,

Delays were due to problems with manufacturing the lift in Germany, followed then by technical difficulties in creating a firm foundation on which to place the lift,

the contractors are now finally able to make progress in the installation.

The cage structure is currently being installed,

once this has been completed, the lift itself will be installed.



All efforts are being made to hasten the process as much as possible. We would love to complete the lift in time for the carol service in December; however the lift contractor has been unable to promise that it will be finished by 17th December. We will, of course, be keeping up the pressure to ensure that it is completed as soon as possible
